

Memo

To: Bethpage Residents
From: Edward Hannon, Project Director
Date: Tuesday, November 2, 2021; 3:30 p.m.
Subject: RW-21 Piping installation (November 3 and 4)
S. Pershing Avenue/Brenner Avenue closure
Central Avenue (N. Herman/Seaman Avenue crossing) traffic control setup begins 11/3
William Street (dead end) conduit installation starts 11/5

Northrop Grumman is providing this progress report to you on the installation of piping to support the RW-21 groundwater treatment system project. Our contractors continue to conduct road work on town- and county-owned streets along the piping route.

We want to thank everyone on S. Pershing Avenue and Brenner Avenue for continuing to move their vehicles during work hours. We ask that everyone on the east side of William Street continue to avoid parking at the dead end while we install conduit over the next two weeks. That work will commence 11/5.

We estimate that by the end of this week (11/5), we will be on Brenner working towards the Sheridan/Brenner intersection, and complete paving restoration on the S. Pershing Avenue segment to open the roadway (with the exception of the intersection of S. Pershing and Brenner). As a reminder, our crew will be inspecting the piping installation route and we will correct any settling of asphalt along the route in the coming two weeks.

Our schedule through November 3 is as follows:


Wednesday, November 3: Our S. Pershing/Brenner Avenue crew will continue trench excavation/shoring, pipe installation, backfilling and paving. Our second crew is tentatively scheduled to initiate setup of traffic control signage on Central Avenue (at Seaman Avenue/N. Herman Avenue crossing). Work will be completed by 4:30 p.m.

Thursday, November 4: Our S. Pershing/Brenner Avenue crew will continue trench excavation/shoring, pipe installation, backfilling, and paving. Our second crew is tentatively scheduled to initiate test pitting on Central Avenue (at Seaman Avenue/N. Herman Ave crossing), with intermittent lane closures as we move through the work zone. Work will be completed by 4:30 p.m.

Upcoming Central Avenue work (at N. Herman Avenue and Seaman Avenue): We anticipate asphalt cutting to begin November 11 (with intermittent lane closures). We expect to begin trenching on November 12 (to expose the existing piping connections at the Seaman Avenue and N. Herman intersections). This will require us to close each of those intersections and there will be intermittent lane closures on Central Avenue in the work zone. The schedule for this work is weather dependent. Drivers who use Central Avenue regularly are advised to use alternative routes to avoid traffic delays at the Seaman Avenue/North Herman Avenue crossing while this work is in progress. Timing to complete this work is weather dependent.

Upcoming Central Avenue work (at Grumman Road East/Hickey Blvd): Work on the Central Avenue crossing of Grumman Road East/Hickey Blvd. to Sheridan will follow the completion of the Seaman Avenue/ N. Herman Avenue crossing. We expect that work to take about 30 days. More details are forthcoming.

ORANGE LINE IS CURRENT WORK ZONE; Black line is completed work.

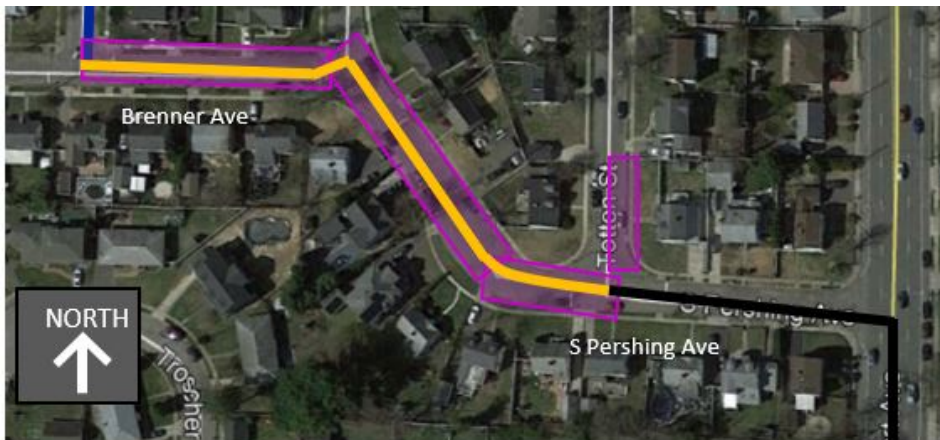

Safe driving and walking through work zones:

Please continue to walk or drive safely around our work zones. S. Pershing Avenue is closed between Brenner Avenue and Totten St (except for the residents who reside within those street sections).

Updates to Bethpage School District Walkers/Bus Routes:

We are incorporating guidance from the transportation office into our upcoming operations.

Work vehicles moving in and out of our staging area:

You may also observe our equipment vehicles entering and exiting our staging area off Broadway south of Arthur Avenue.

Please contact **Dianne Baumert-Moyik** via mobile at **(516) 754-2645** or via email at Dianne.baumert-moyik@ngc.com to be added to our email list.

We appreciate everyone's continued support. For project updates, visit www.northropgrumman.com/bethpage. Thank you.
